



CAPITAL IMPROVEMENT PROJECTS INFORMATION

D STREET PAVING PROJECT

Planned Start Date: 6/1/2014

Planned End Date: 12/23/2015

Project Type: PAVING

Project Limits: Douglas Ave. to Storey Ave.

Project Phase: **Completed**



Next Activity: Project Complete

Opinion of Probable Cost: \$1,500,000.00

Authorized Funding Amount: \$1,945,803.15

Construction Cost: \$1,927,652.45

Project Photo:



Project Scope: Pave the street and install new storm drain.


Point of Contact: Matt Carr, P.E.
432-685-7415
mcarr@midlandtexas.gov

Design: In-house Project
432-685-7287
Engineering Services


Contractor: Reece Albert, Inc.
7600 N. County Road 1150
Midland, Texas 79705

Comments: Project completed on time and on budget.

Vicinity Map:

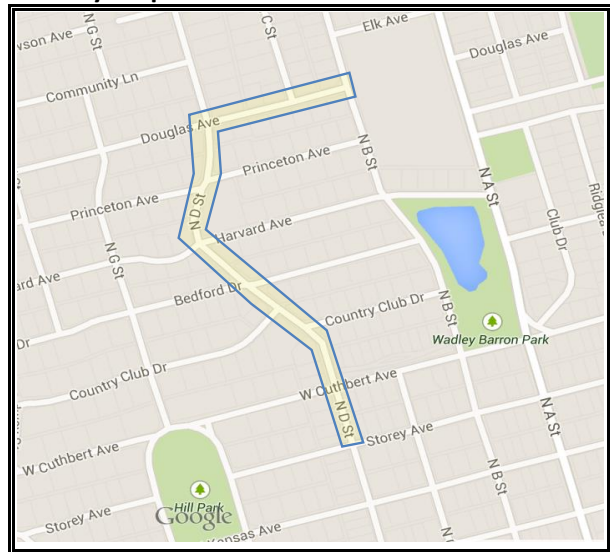

Project Schedule:



Legend - [Yellow] Survey [Blue] Plan [Green] Design [Red] Delay [Purple] Bid [Orange] Construction [Grey] Time
